BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	: Executive Engineer Yelahanka Division
Project Name	: CONSTRUCTION OF COMPOUND WALL AND OTHER ALLIED WORKS AT JUDICIAL LAYOUT PLAY GRO
Consultants	: Civil Pro
Project Manager /Team Leader	: Karthik Rechan
Project Start Date	: 11-Aug-21
Project End Date	: 30-Jul-22
Project Length in Months	: 11 months

Sl No	*Assignment*	*Unit*	*Tender Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
1	Earthwork excavation for foundation of buildings, water supply, sanitary lines and electrical conduits either in pits or in trenches 1.5m and above in width, in hard soil not	Cum	4505 90	4505 90	100	12-08-21	22-08-21	10
2	Providing and laying in position plain cement concrete of mix 1 3 6 with OPC cement @ 220kgs, with 40mm and down size graded granite metal coarse aggregates @0 892cum and fine aggregates @ 0 465cum machine	Cum	111 26	111 26	100	05-09-21	15-09-21	10
3	Providing and Filling in foundation with granite / trap broken metal 100mm and down size, with approved sand including hand	Cum	148 35	148 35	100	24-08-21	03-09-21	10
4	Providing T.M.T bars Fe 500 steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and	Tonne	97 01	97 01	100	18-09-21	08-10-21	20
5	Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for vertical surface such as walls at any thickness, including attached pilasters,	Sqm	1752 83	1752 83	100	09-10-21	29-10-21	20
	Providing Weep Holes KSRRB M2200-8. Providing weep holes in Brick masonry / Plain / Reinforced concrete abutment, wing wall / return wall with 100 mm dia AC pipe, extending through the full width of the structure	Nos/mtr	135 00	135 00	100	31-10-21	02-11-21	2
	Providing and laying in position reinforced cement concrete of design mix M25 with OPC cement @ 340kgs, with 20mm and down size graded granite metal coarse aggregates	Cum	12 15	12 15	100	03-11-21	05-11-21	2
	Providing and laying in position reinforced cement concrete of design mix M25 with OPC cement @ 340kgs, with 20mm and down size graded granite metal coarse aggregates @0 70cum and fine aggregtes @ 0 47cum, with	Cum	769 96	769 96	100	05-11-21	17-11-21	12
	Filling available excavated earth (excluding rock) in sides of foundations upto plinth in layers not exceeding 20 cms. in depth, compacting each deposited layer by ramming	Cum	3808 21	3808 21	100	18-11-21	30-11-21	12
	Conveying the excavated earth, debries etc., with all lead and lifts including loading and unloading charges etc., complete as per the	Cum	695 38	695 38	100	02-12-21	10-12-21	8

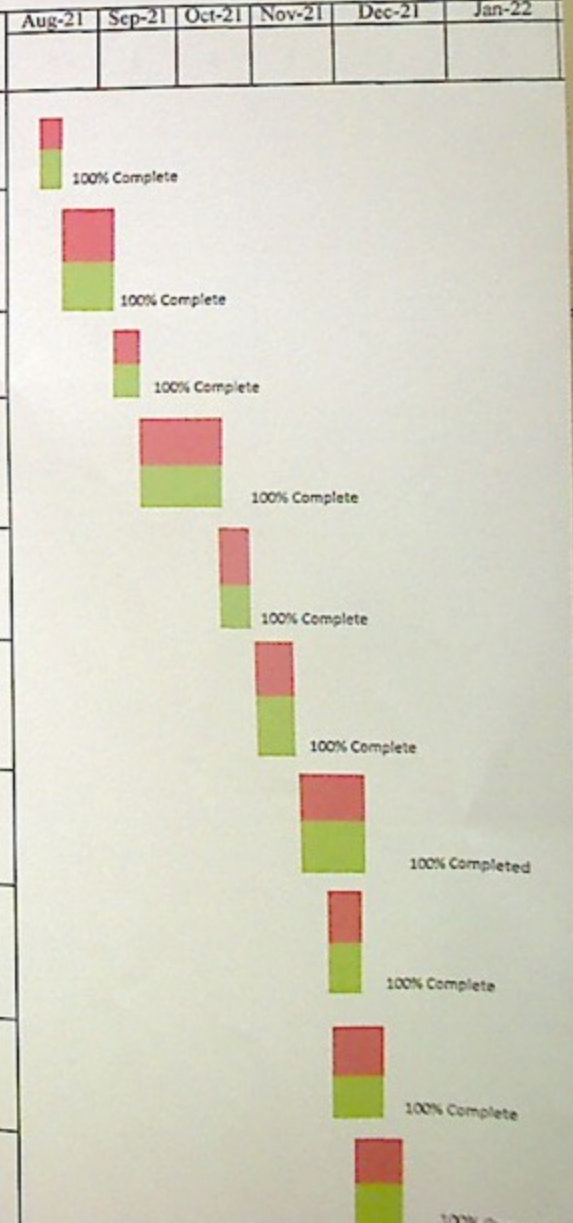

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	CONSTRUCTION OF COMPOUND WALL AND OTHER ALLIED WORKS AT JUDICIAL LAYOUT PLAY GROUND IN WAR
Consultants	:	Civil Pro
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	11-Aug-21
Project End Date	:	30-Jul-22
Project Length in Months	:	11 months

SL No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
11	Supply and Installation of approved Wooden Floor for Indoor Hall - Maple Flooring with PU Scaler and coat polish 20mm,thickness*60mm width*2000mm, third &better grade treated sleepers of size 30*60mm to be installed 30cm center to center 20mmm professional EPDM rubber pad inclusive of HOM, labour etc. asper	Sqm	149.42	149.42	100	12-12-21	16-12-21	4
11	Supply and Installation of approved Wooden Floor for Indoor Hall - Maple Flooring with PU Scaler and coat polish 20mm,thickness*60mm width*2000mm, third &better grade treated sleepers of size 30*60mm to be installed 30cm center to center 20mmm professional EPDM rubber pad inclusive of HOM, labour etc. asper	Sqm	149.42	149.42	100	12-12-21	16-12-21	4
12	Providing and fixing of Aluminium composite panel of approved make and colour for wall cladding for curved Brick/Rcc/stone walls & coloumns/beams with necessary aluminium frame works at required level made out of 50x25x3mm C section or equalent. The panel should consist of 2.5 mm thermoplastic core of	Sqm	187.38	187.38	100	01-01-22	30-07-22	210

ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ.
ಜ.ಜ.ಪಾ.ಮ. ಬೆಂಗಳೂರು-106
